


AMR PROGRESS PER MINISUB

MINISUB	RATING	BULK ON AMR	KIOSKS	SUPPLIES	INSTALLED	ORDERED	OUTSTANDING	DEFERRED	% ON AMR	
MS 01	500 kVA (800A)	Yes	15	67	0	0	67	0	0%	
MS 02	500 kVA (800A)	No	8	41	0	0	41	0	0%	
MS 03	500 kVA (800A)	Yes	25	119	0	0	119	0	0%	
MS 04	500 kVA (800A)	Yes	11	65	0	0	65	0	0%	
MS 05	315 kVA (500A)	Yes	9	41	0	0	41	0	0%	
MS 06	500 kVA (800A se	Yes	15	89	0	0	89	0	0%	
MS 07	315 kVA (450A)	No	0	2	0	0	2	0	0%	
MS 08	315 kVA (450A)	No	8	46	0	0	46	0	0%	
MS 09	500 kVA (800A se	No	16	78	0	0	78	0	0%	
MS 10	500 kVA (800A se	No	0	1	0	0	1	0	0%	
MS 11	500 kVA (800A se	No	0	1	0	0	1	0	0%	
MS 12	500 kVA (800A se	No	0	1	0	0	1	0	0%	
MS 13	315 kVA (450A)	No	6	30	0	0	30	0	0%	
MS 14	500 kVA (800A se	No	4	19	0	0	19	0	0%	
MS 15	500 kVA (800A se	No	10	54	0	0	54	0	0%	
TOTAL				654	0	0	654	0	0%	

KEY PLAN (from KMZ) – square colour: green = AMR started/complete, amber = in current order, red = not started

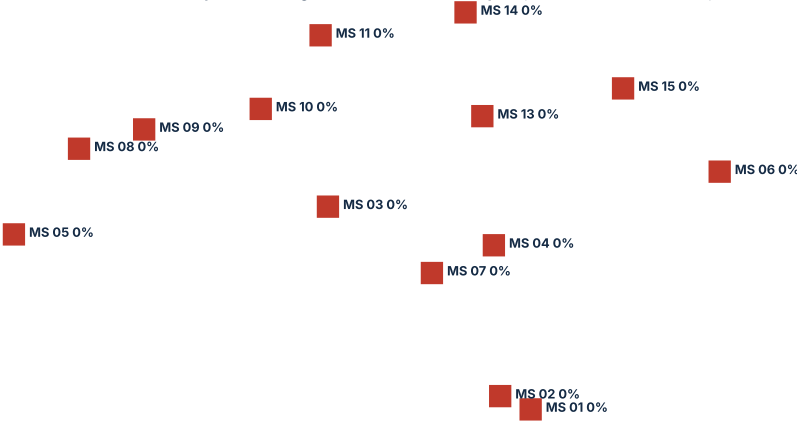

Notes: 1) Supply = one metered connection (1 probe). Future PUD sites are not counted as supplies. 2) Kiosk feeds not stated in the sheet are inferred from the sheet layout (dashed) – verify against as-built SLDs.

3) Status colours: green = on AMR, amber = on an open order, red = outstanding, grey = deferred.



AMR PROGRESS (supplies)

0% on AMR



Installed 0 Ordered 0 Outstanding 654 Deferred 0

SEATON ESTATE

SITE OVERVIEW – AMR PROGRESS PER MINISUB

Supplies per minisub from the master hierarchy workbook.

— feed per sheet - - - - - inferred from layout Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No. SEA-SLD-00	REVISION A	
DATE 2026-10-09	SCALE NTS	
DRAWN Ruan van Heerden, Electrical Engineer		SHEET 1 of 16

MS 01


500 kVA (800A)

Bulk 91074351

Bulk on AMR

Direct from LV board:

■ MZL 01 - S/L · 80A (RWB) · 91073505

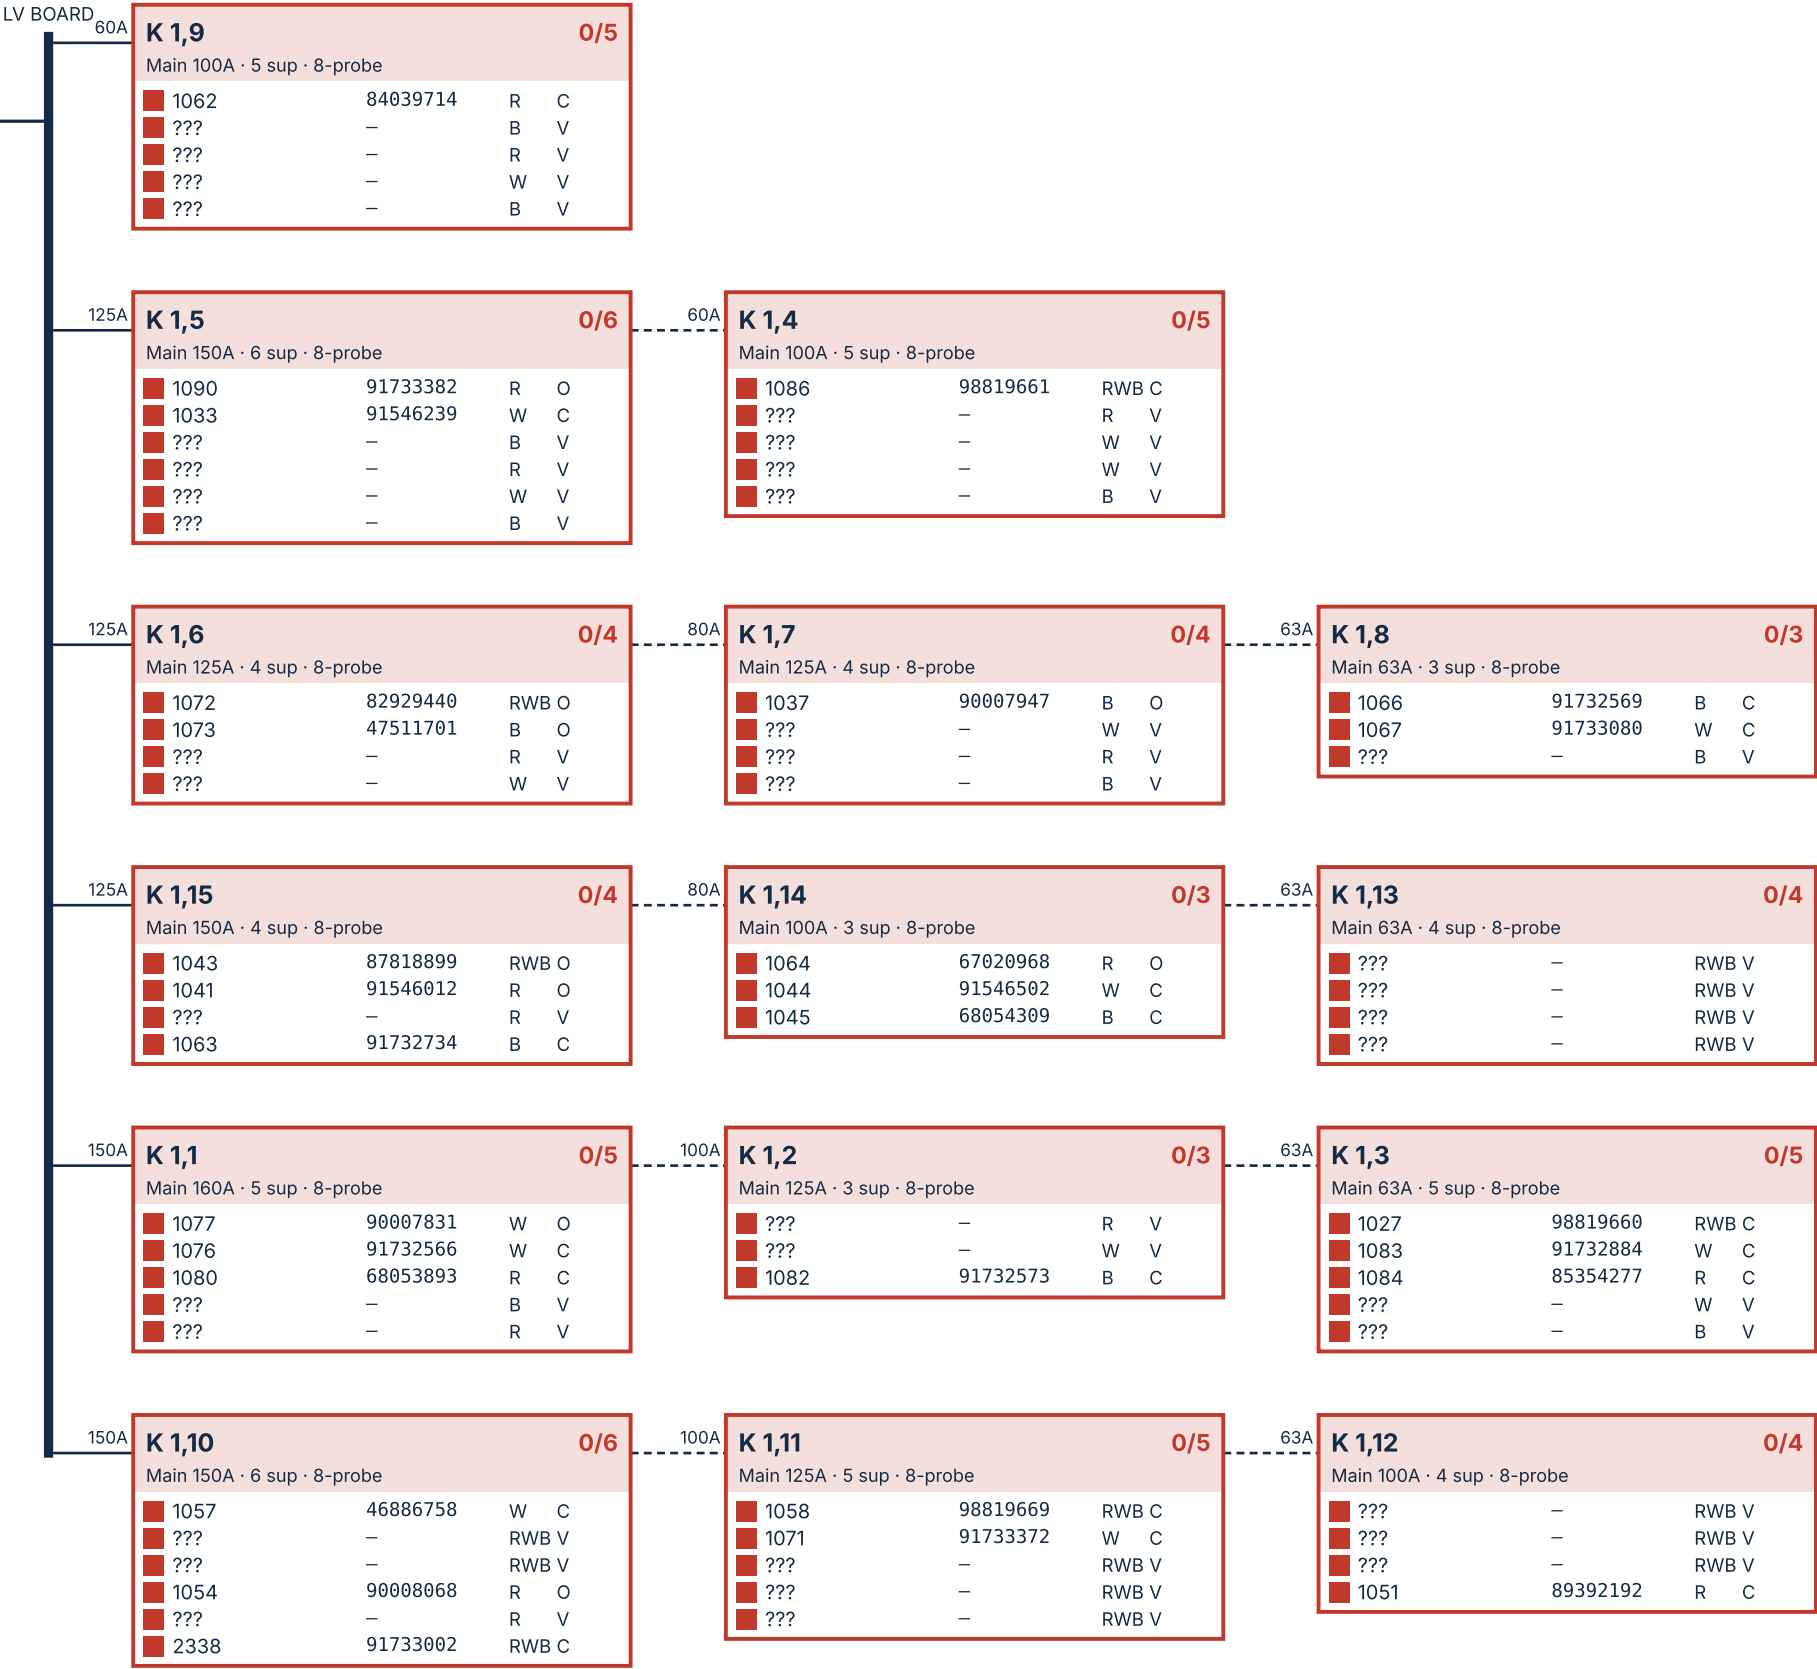

MS 02

500 kVA (800A)

Bulk 83183211

Bulk NOT on AMR

Direct from LV board:

1094 - Seranno · 225A · –



K 2,10/3				
Main 100A · 3 sup · 8-probe				
1091	–	–	V	
1092	68054291	R	C	
1093	–	–	V	

K 2,30/4				
Main 100A · 4 sup · 8-probe				
–	–	–	?	
–	–	–	?	
–	–	–	?	
–	–	–	?	

FEED NOT CONFIRMED IN SHEET – placement only

K K-SSM0/3				
Main 225A · 3 sup · 8-probe				
Entrance Sign	–	R	O	
K-SS 2	–	RWB	O	
K-SS 1	–	RWB	O	

K K-SS 10/9				
Main 125A · 9 sup · 16-probe				
BL A Unit 01	91546217	R	C	
BL A Unit 02	91546285	R	C	
BL A Unit 03	91546316	W	C	
BL A Unit 04	91546291	B	C	
BL A Unit 05	91546184	R	C	
BL A Unit 06	91546336	W	C	
BL A Unit 07	91546292	B	C	
BL A Unit 08	91546215	R	C	
Communal	–	–	O	

K K-SS 20/6				
Main 175A · 6 sup · 8-probe				
BL B Unit 09	91733102	R	C	
BL B Unit 10	91546310	W	C	
BL B Unit 11	91546284	B	C	
BL B Unit 12	91546210	R	C	
BL B Unit 13	91546286	W	C	
BL B Unit 14	91546261	B	C	

125A

K K-SS 30/7				
Main 125A · 7 sup · 8-probe				
BL C Unit 15	91546209	R	C	
BL C Unit 16	91733106	W	C	
BL C Unit 17	91546266	B	C	
BL C Unit 18	91546179	R	C	
BL C Unit 19	91546236	W	C	
BL D Unit 20	91546190	B	C	
BL D Unit 21	91546293	R	C	

K 2,40/4				
Main 100A · 4 sup · 8-probe				
–	–	–	?	
–	–	–	?	
–	–	–	?	
–	–	–	?	

K 2,50/4				
Main 100A · 4 sup · 8-probe				
–	–	–	?	
–	–	–	?	
–	–	–	?	
–	–	–	?	

KIOSK AMR SCHEDULE

KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone
K 2,1	3	0	0	3	8-probe
K K-SSM	3	0	0	3	8-probe
K K-SS 1	9	0	0	9	16-probe
K K-SS 2	6	0	0	6	8-probe
K K-SS 3	7	0	0	7	8-probe
K 2,3	4	0	0	4	8-probe
K 2,4	4	0	0	4	8-probe
K 2,5	4	0	0	4	8-probe



AMR PROGRESS (supplies)

0% on AMR



Installed 0 Ordered 0 Outstanding 41 Deferred 0

SEATON ESTATE

MS 02 – LV RETICULATION & AMR STATUS

SGB - Smit Power Matla · 500 kVA (800A) · mfd 03/2022 · bulk meter 83183211 (not on AMR)

— feed per sheet - - - - - inferred from layout Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-02	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	3 of 16	

MS 03

500 kVA (800A)

Bulk 83183198

Bulk on AMR

Direct from LV board:

Seaton Irrigation - 63A (RWB) - 87818942

MS 03 - LV & S/L - 250A - -





MS 05

315 kVA (500A)

Bulk 91074352

Bulk on AMR

- Direct from LV board:
- Main G/H, Substation & · 125A · 90915180
 - MS 05 - S/L · 80A (RWB) · 91073486



MS 06

500 kVA (800A set to 750A)

Bulk 90915181

Bulk on AMR

- Direct from LV board:
- Streetlights SL 6,1 - 32A - 63236959
 - B/H Main DB - 100A (35mm) - 63236950



MS 07

315 kVA (450A)

Bulk 91073764

Bulk NOT on AMR



- Direct from LV board:
- Field Lights · 150A · –
 - Sports Club · 200A · –

KIOSK AMR SCHEDULE

KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	2	0	0	2	8-probe



AMR PROGRESS (supplies)

0% on AMR



Installed 0 Ordered 0 Outstanding 2 Deferred 0

SEATON ESTATE

MS 07 – LV RETICULATION & AMR STATUS

Electronic Assemblies (PTY) Ltd. · 315 kVA (450A) · mfd 2025 · bulk meter 91073764 (not on AMR)

— feed per sheet - - - - - inferred from layout Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-07	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN		SHEET
Ruan van Heerden, Electrical Engineer		8 of 16


MS 08


315 kVA (450A)

Bulk 98820120

Bulk NOT on AMR

- Direct from LV board:
- Streetlights SL 8,1 · 32A · 62639802
 - Main Gatehouse · 63A · –

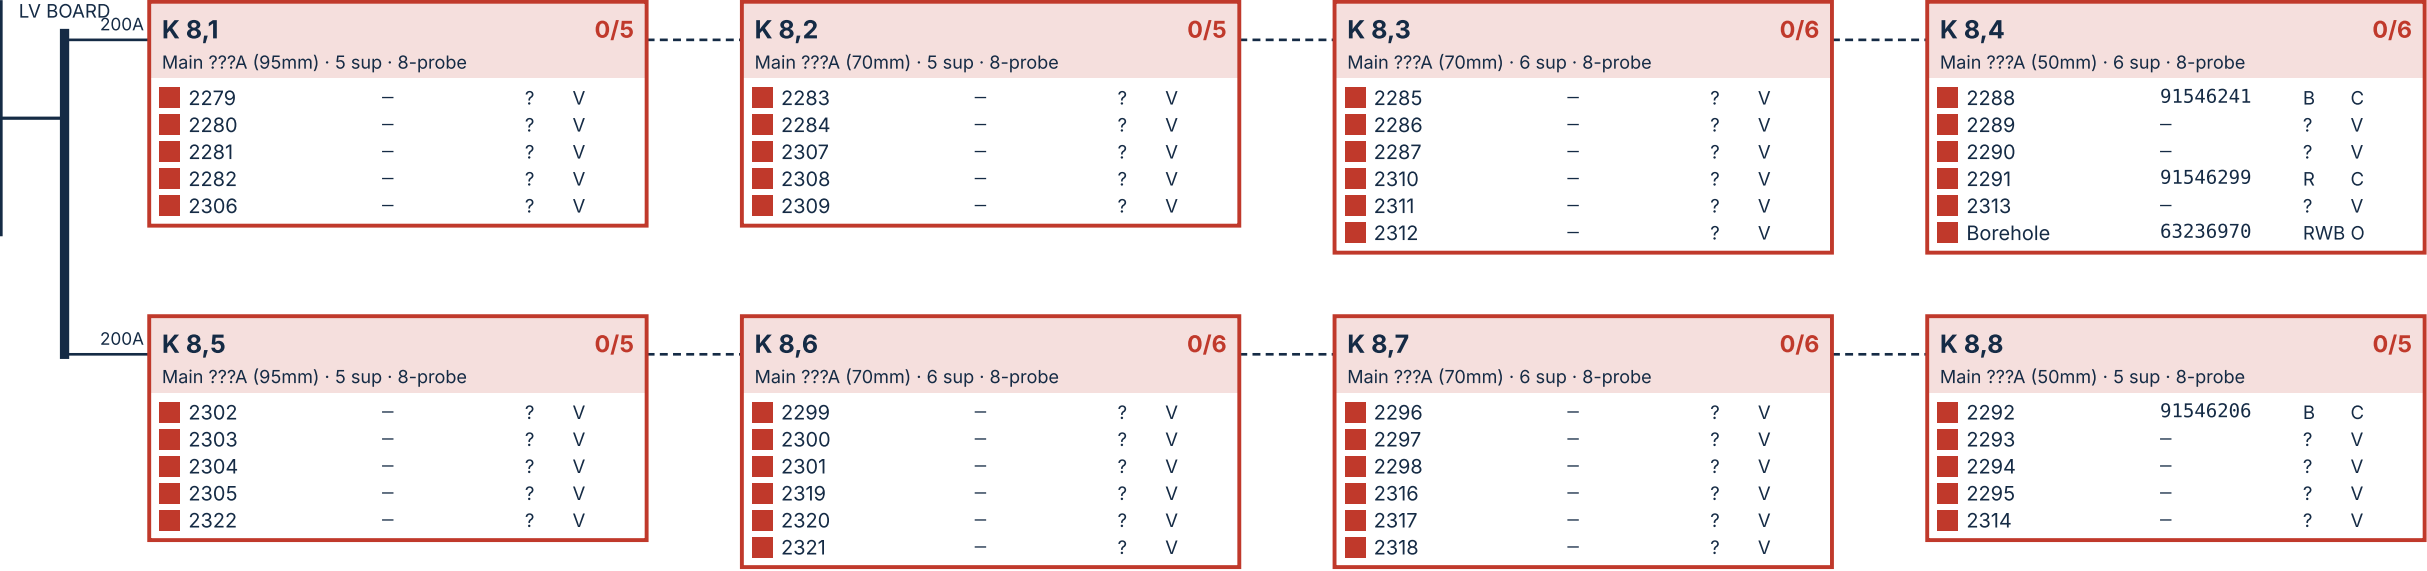

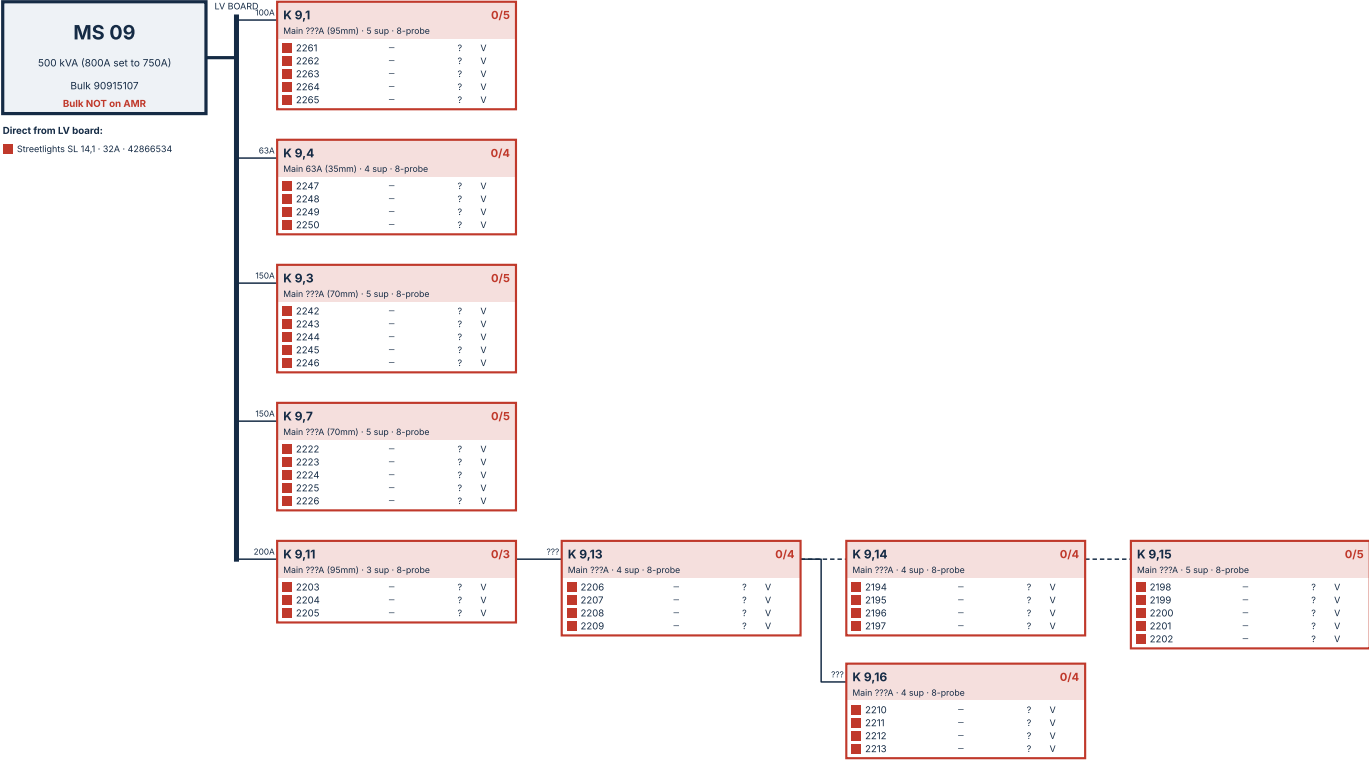

FEED NOT CONFIRMED IN SHEET – placement only

K 9,2	0/5	Main 777A (35mm) · 5 sup · 8-probe
2256	–	? V
2257	–	? V
2258	–	? V
2259	91732378	B C
2260	91732362	R C

K 9,5	0/6	Main 777A (50mm) · 6 sup · 8-probe
2238	–	? V
2239	91546228	R C
2240	–	? V
2241	–	? V
2251	–	? V
2252	–	? V

K 9,6	0/7	Main 777A (50mm) · 7 sup · 8-probe
2234	–	? V
2235	91546620	B C
2236	–	? V
2237	–	? V
2253	67828686	R C
2254	98867848	W C
2255	67828999	R C

K 9,8	0/4	Main 777A (70mm) · 4 sup · 8-probe
2220	–	? V
2221	–	? V
2227	91733853	R C
2228	–	? V

K 9,9	0/5	Main 777A (70mm) · 5 sup · 8-probe
2217	–	? V
2218	–	? V
2219	–	? V
2229	–	? V
2230	–	? V

K 9,10	0/6	Main 777A (50mm) · 6 sup · 8-probe
2214	–	? V
2215	68854897	R C
2216	–	? V
2231	–	? V
2232	–	? V
2233	–	? V

K 9,12	0/5	Main 777A · 5 sup · 8-probe
2189	68853856	B C
2190	–	? V
2191	–	? V
2192	–	? V
2193	–	? V

KIOSK AMR SCHEDULE

KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone
K 9,1	5	0	0	5	8-probe
K 9,2	5	0	0	5	8-probe
K 9,4	4	0	0	4	8-probe
K 9,3	5	0	0	5	8-probe
K 9,5	6	0	0	6	8-probe
K 9,6	7	0	0	7	8-probe
K 9,7	5	0	0	5	8-probe
K 9,8	4	0	0	4	8-probe
K 9,9	5	0	0	5	8-probe
K 9,10	6	0	0	6	8-probe
K 9,11	3	0	0	3	8-probe
K 9,12	5	0	0	5	8-probe
K 9,13	4	0	0	4	8-probe
K 9,14	4	0	0	4	8-probe
K 9,15	5	0	0	5	8-probe
K 9,16	4	0	0	4	8-probe



AMR PROGRESS (supplies)

0% on AMR



Installed 0 Ordered 0 Outstanding 78 Deferred 0

SEATON ESTATE

MS 09 – LV RETICULATION & AMR STATUS


Electronic Assemblies (PTY) Ltd. · 500 kVA (800A set to 750A) · mfd 2024 · bulk meter 90915107 (not on AMR)

— feed per sheet - - - - - inferred from layout Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION
SEA-SLD-09	A
DATE	SCALE
2026-10-09	NTS
DRAWN	SHEET
Ruan van Heerden, Electrical Engineer	10 of 16



KIOSK AMR SCHEDULE					
KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone



SEATON ESTATE

MS 10 – LV RETICULATION & AMR STATUS

Electronic Assemblies (PTY) Ltd. · 500 kVA (800A set to 750A) · mfd 2024 · bulk meter 98820124 (not on AMR)

— feed per sheet

----- inferred from layout

Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-10	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	11 of 16	

MS 11

500 kVA (800A set to 750A)

Bulk 91073762


Bulk NOT on AMR

Direct from LV board:

Streetlights SL 11,1 · 32A · 64126541



KIOSK AMR SCHEDULE					
KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone



SEATON ESTATE

MS 11 – LV RETICULATION & AMR STATUS


Electronic Assemblies (PTY) Ltd. · 500 kVA (800A set to 750A) · mfd 2024 · bulk meter 91073762 (not on AMR)

— feed per sheet

----- inferred from layout

Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-11	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	12 of 16	



Direct from LV board:

Streetlights SL 12,1 · 32A · 63236961

KIOSK AMR SCHEDULE					
KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone



AMR PROGRESS (supplies)

0% on AMR

Installed 0

Ordered 0

Outstanding 1

Deferred 0

SEATON ESTATE

MS 12 – LV RETICULATION & AMR STATUS

Electronic Assemblies (PTY) Ltd. · 500 kVA (800A set to 750A) · mfd 2024 · bulk meter 98820129 (not on AMR)

— feed per sheet

----- inferred from layout

Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-12	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	13 of 16	

MS 13

315 kVA (450A)

Bulk 98820126

Bulk NOT on AMR

Direct from LV board:

Streetlights SL 13,1 · 32A · 63236904

LV BOARD

63A

K 13,1

Main 63A (50mm) · 7 sup · 8-probe

2135

2136

2137

2138

2139

2140

2141

—

—

—

91732558

—

—

—

?

?

?

W

?

?

?

V

V

V

C

V

V

V

0/7

125A

K 13,5

Main ???A (70mm) · 3 sup · 8-probe

2116

2117

2118

—

—

—

?

?

?

V

V

V

0/3

K 13,6

Main ???A (50mm) · 3 sup · 8-probe

2106

2107

2115

—

—

—

?

?

?

V

V

V

0/3

K 13,7

Main ???A (50mm) · 7 sup · 8-probe

2108

2109

2110

2111

2112

2113

2114

—

—

—

—

—

—

—

?

?

?

?

?

?

?

V

V

V

V

V

V

V

0/7

125A

K 13,3

Main ???A (50mm) · 5 sup · 8-probe

2119

2120

2132

2133

2134

—

—

—

—

—

?

?

?

?

?

V

V

V

V

V

0/5

K 13,4

Main ???A (50mm) · 4 sup · 8-probe

2121

2122

2130

2131

—

—

—

—

?

?

?

?

V

V

V

V

0/4

200A

K 13,2

Main 200A (70mm)

LV

KIOSK AMR SCHEDULE

KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone
K 13,1	7	0	0	7	8-probe
K 13,5	3	0	0	3	8-probe
K 13,6	3	0	0	3	8-probe
K 13,7	7	0	0	7	8-probe
K 13,3	5	0	0	5	8-probe
K 13,4	4	0	0	4	8-probe



AMR PROGRESS (supplies)

0% on AMR



Installed 0 Ordered 0 Outstanding 30 Deferred 0

SEATON ESTATE

MS 13 – LV RETICULATION & AMR STATUS

Electronic Assemblies (PTY) Ltd. · 315 kVA (450A) · mfd 2024 · bulk meter 98820126 (not on AMR)

— feed per sheet - - - - - inferred from layout Rows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-13	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	14 of 16	

MS 14


500 kVA (800A set to 750A)

Bulk 98820123

Bulk NOT on AMR

Direct from LV board:

Streetlights SL 14,1 · 32A · 63237000

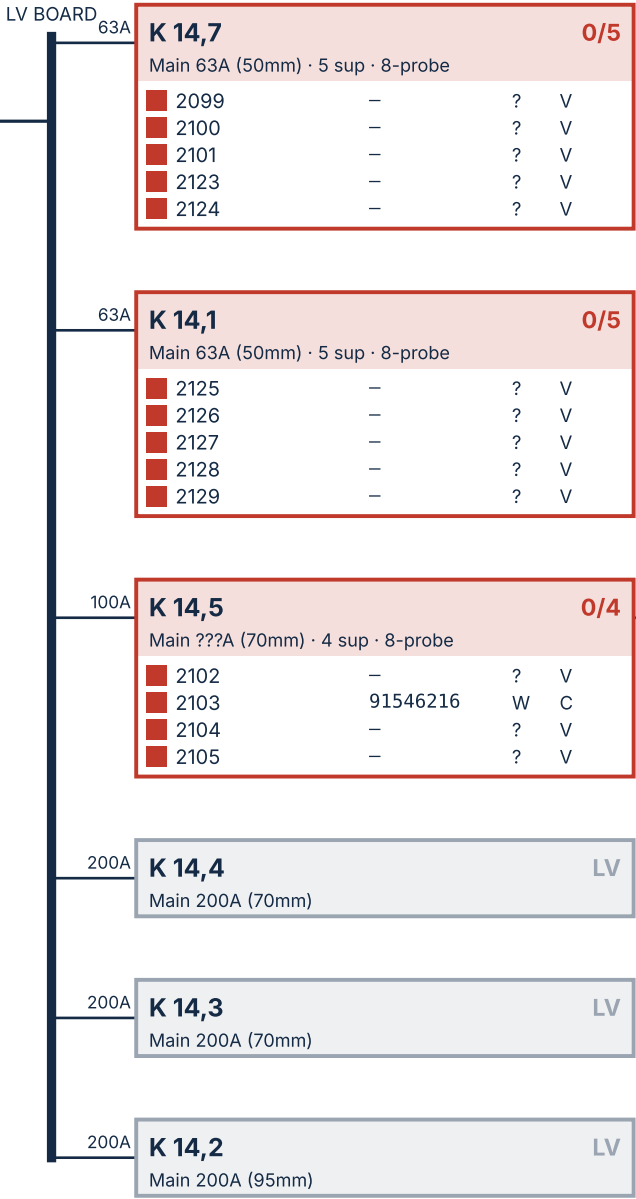

KIOSK AMR SCHEDULE					
KIOSK	SUP	ON AMR	ORD	OUT	UNIT
MS LV board	1	0	0	1	Standalone
K 14,7	5	0	0	5	8-probe
K 14,1	5	0	0	5	8-probe
K 14,5	4	0	0	4	8-probe
K 14,6	4	0	0	4	8-probe



AMR PROGRESS (supplies)

0% on AMR



Installed 0Ordered 0Outstanding 19Deferred 0

SEATON ESTATE

MS 14 – LV RETICULATION & AMR STATUS

Electronic Assemblies (PTY) Ltd. · 500 kVA (800A set to 750A) · mfd 2025 · bulk meter 98820123 (not on AMR)

feed per sheetinferred from layoutRows: status · stand · S/N · ph · Q/C/V · port

DRAWING No.	REVISION	
SEA-SLD-14	A	
DATE	SCALE	
2026-10-09	NTS	
DRAWN	SHEET	
Ruan van Heerden, Electrical Engineer	15 of 16	

MS 15

500 kVA (800A set to 750A)

Bulk 98820127

Bulk NOT on AMR

Direct from LV board:

Streetlights SL 15,1 · 32A · 63236992

